

ansab		Development of the Technology City in Dammam-Project UPDATE 15-09-2026 3Week Lookahead Schedule				egis		MODON مَدِينَة الرياض				
Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost	2026				
								Aug	Sep	Oct	Nov	Dec
Development of the Technology City in Dammam-Project UPDATE 15-09-2026		197	02-Aug-26 A	20-Feb-27	23-Jun-26	19-Jan-27	14,752,597.99					
Key Milestones		0	24-Sep-26	24-Sep-26	13-Jul-26	13-Jul-26	0.00					
Contractual Milestones		0	24-Sep-26	24-Sep-26	13-Jul-26	13-Jul-26	0.00					
MS-CF-ENG	Completion of Submitting and Approval of Shopdrwing and Material	0		24-Sep-26		13-Jul-26	0.00					
Engineering Works		8	15-Sep-26	24-Sep-26	23-Jun-26	02-Jul-26	0.00					
Material Submittals and Approvals		8	15-Sep-26	24-Sep-26	23-Jun-26	02-Jul-26	0.00					
Short Lead Time Items		7	15-Sep-26	22-Sep-26	23-Jun-26	30-Jun-26	0.00					
Superstructure Works		7	15-Sep-26	22-Sep-26	23-Jun-26	30-Jun-26	0.00					
Storage Tank (TSE)		7	15-Sep-26	22-Sep-26	23-Jun-26	30-Jun-26	0.00					
Submission of Material		7	15-Sep-26	22-Sep-26	23-Jun-26	30-Jun-26	0.00					
ENG-MT-TSE-CV-٤	Material Submittal for Civil Works for Storage Tank (TSE)	7	15-Sep-26	22-Sep-26	23-Jun-26	30-Jun-26	0.00					
Long Lead Time Items		8	15-Sep-26	24-Sep-26	24-Jun-26	02-Jul-26	0.00					
Superstructure Works		8	15-Sep-26	24-Sep-26	24-Jun-26	02-Jul-26	0.00					
Pump Stations		8	15-Sep-26	24-Sep-26	24-Jun-26	02-Jul-26	0.00					
Submission of Material		7	15-Sep-26	22-Sep-26	24-Jun-26	01-Jul-26	0.00					
ENG-MT-SPS-MC-	Material Submittal for Electromechanical Works for Pump Stations	7	15-Sep-26	22-Sep-26	24-Jun-26	01-Jul-26	0.00					
Approval of Material		8	15-Sep-26	24-Sep-26	24-Jun-26	02-Jul-26	0.00					
ENG-MT-SPS-MC-	Material Approval for Electromechanical Works for Pump Stations	8	15-Sep-26	24-Sep-26	24-Jun-26	02-Jul-26	0.00					
Storage Tank (TSE)		8	15-Sep-26	24-Sep-26	24-Jun-26	02-Jul-26	0.00					
Submission of Material		7	15-Sep-26	22-Sep-26	24-Jun-26	01-Jul-26	0.00					
ENG-MT-TSE-MC-٤	Material Submittal for Electromechanical Works for Storage Tank (TSE)	7	15-Sep-26	22-Sep-26	24-Jun-26	01-Jul-26	0.00					
Approval of Material		8	15-Sep-26	24-Sep-26	24-Jun-26	02-Jul-26	0.00					
ENG-MT-TSE-MC-٤	Material Approval for Electromechanical Works for Storage Tank (TSE)	8	15-Sep-26	24-Sep-26	24-Jun-26	02-Jul-26	0.00					
Procurement Cycle		184	02-Aug-26 A	20-Feb-27	23-Jun-26	12-Dec-26	0.00					
Short Lead Time Items		184	02-Aug-26 A	20-Feb-27	23-Jun-26	12-Dec-26	0.00					
Infrastructure Networks		184	02-Aug-26 A	20-Feb-27	23-Jun-26	12-Dec-26	0.00					
Road Works		40	02-Aug-26 A	15-Sep-26	02-Nov-26	05-Dec-26	0.00					
Material Delivery & Site Inspection		40	02-Aug-26 A	15-Sep-26	02-Nov-26	05-Dec-26	0.00					
Pre-Bituminous Construction		40	02-Aug-26 A	15-Sep-26	02-Nov-26	12-Nov-26	0.00					
PRO-R25-RD-DL-٢	Material Delivery & Site Inspection for Subgrade of Road Works	0	02-Aug-26 A	15-Sep-26	02-Nov-26	02-Nov-26	0.00					
PRO-R25-RD-DL-٢	Material Delivery & Site Inspection for Aggregate Base Course of Road Works	0	15-Sep-26	15-Sep-26	12-Nov-26	12-Nov-26	0.00					
Bituminous Construction		0	15-Sep-26	15-Sep-26	05-Dec-26	05-Dec-26	0.00					
PRO-R25-RD-DL-٢	Material Delivery & Site Inspection for Prime Coat of Road Works	0	15-Sep-26	15-Sep-26	05-Dec-26	05-Dec-26	0.00					
PRO-R25-RD-DL-٢	Material Delivery & Site Inspection for Bituminous Base & Wearing Courses of Road	0	15-Sep-26	15-Sep-26	05-Dec-26	05-Dec-26	0.00					
Pavement Works		0	15-Sep-26	15-Sep-26	12-Nov-26	12-Nov-26	0.00					
PRO-R25-RD-DL-٢	Material Delivery & Site Inspection of Interlock Tiles for Landscaping	0	15-Sep-26	15-Sep-26	12-Nov-26	12-Nov-26	0.00					
PRO-R25-RD-DL-٢	Material Delivery & Site Inspection of Curbstones for Landscaping	0	15-Sep-26	15-Sep-26	12-Nov-26	12-Nov-26	0.00					
Traffic Signs Boards and Roads Marking		0	15-Sep-26	15-Sep-26	08-Nov-26	25-Nov-26	0.00					
PRO-R25-RD-DL-٢	Material Delivery & Site Inspection of Traffic Signs Boards For Road Works	0	15-Sep-26	15-Sep-26	08-Nov-26	08-Nov-26	0.00					
PRO-R25-RD-DL-٢	Material Delivery & Site Inspection of Road Markings For Road Works	0	15-Sep-26	15-Sep-26	25-Nov-26	25-Nov-26	0.00					
Softscape and Planting Works		82	15-Sep-26	20-Dec-26	11-Jul-26	17-Oct-26	0.00					
Issuance of Purchase Orders		6	15-Sep-26	21-Sep-26	11-Jul-26	19-Jul-26	0.00					
Main Line Pipes		6	15-Sep-26	21-Sep-26	11-Jul-26	19-Jul-26	0.00					
PRO-IR-PO-140	Issuance of Purchase Order for Softscape and Planting Works	6	15-Sep-26	21-Sep-26	12-Jul-26	19-Jul-26	0.00					
PRO-IR-PO-150	Issuance of Purchase Order for Site Furnishings (Seating Bench,Stone Boulders and	6	15-Sep-26	21-Sep-26	11-Jul-26	18-Jul-26	0.00					
Manufacturing of Material		90	22-Sep-26	20-Dec-26	18-Jul-26	17-Oct-26	0.00					
Main Line Pipes		90	22-Sep-26	20-Dec-26	18-Jul-26	17-Oct-26	0.00					
PRO-IR-MF-140	Manufacturing of Softscape and Planting Works	90	22-Sep-26	20-Dec-26	19-Jul-26	17-Oct-26	0.00					
PRO-IR-MF-150	Manufacturing of Valves for Site Furnishings (Seating Bench,Stone Boulders and Gr	90	22-Sep-26	20-Dec-26	18-Jul-26	16-Oct-26	0.00					
Sewage Network		116	15-Sep-26	29-Jan-27	08-Jul-26	21-Nov-26	0.00					
Issuance of Purchase Orders		6	15-Sep-26	21-Sep-26	08-Jul-26	14-Jul-26	0.00					
Testing and Finishes		6	15-Sep-26	21-Sep-26	08-Jul-26	14-Jul-26	0.00					
Primary Baseline Remaining Work Critical Remaining Work Actual Work Baseline Milestone Milestone Summary								Date	Revision	Checked	Approved	
								15-Sep-26	Third Industrial City			

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost	2026				
								Aug	Sep	Oct	Nov	Dec
PRO-SW-PO-120	Issuance of Purchase Order for Manhole Covers of Sewage Network	6	15-Sep-26	21-Sep-26	08-Jul-26	14-Jul-26	0.00					
Manufacturing of Material		130	22-Sep-26	29-Jan-27	15-Jul-26	21-Nov-26	0.00					
Testing and Finishes		130	22-Sep-26	29-Jan-27	15-Jul-26	21-Nov-26	0.00					
PRO-SW-MF-120	Manufacturing of Manhole Covers for Sewage Network	130	22-Sep-26	29-Jan-27	15-Jul-26	21-Nov-26	0.00					
Material Delivery & Site Inspection		0	15-Sep-26	15-Sep-26	09-Aug-26	09-Aug-26	0.00					
Main Line Sections		0	15-Sep-26	15-Sep-26	09-Aug-26	09-Aug-26	0.00					
PRO-R25-SW-DL-	Material Delivery & Site Inspection of Manholes for Sewage Network	0	15-Sep-26	15-Sep-26	09-Aug-26	09-Aug-26	0.00					
Storm Drainage Network		143	02-Aug-26 A	30-Dec-26	23-Jun-26	22-Oct-26	0.00					
Issuance of Purchase Orders		6	15-Sep-26	22-Sep-26	23-Jun-26	14-Jul-26	0.00					
Main Line Sections		6	15-Sep-26	22-Sep-26	23-Jun-26	01-Jul-26	0.00					
PRO-SD-PO-100	Issuance of Purchase Order for Manholes of Storm Drainage Network	6	15-Sep-26	22-Sep-26	23-Jun-26	30-Jun-26	0.00					
PRO-SD-PO-110	Issuance of Purchase Order for Main Line Pipes of Storm Drainage Network	3	15-Sep-26	17-Sep-26	28-Jun-26	01-Jul-26	0.00					
Catch Basin Sections		6	15-Sep-26	21-Sep-26	23-Jun-26	29-Jun-26	0.00					
PRO-SD-PO-130	Issuance of Purchase Order for Catch Basins of Storm Drainage Network	6	15-Sep-26	21-Sep-26	23-Jun-26	29-Jun-26	0.00					
PRO-SD-PO-150	Issuance of Purchase Order for Catch Basin Pipes of Storm Drainage Network	6	15-Sep-26	21-Sep-26	23-Jun-26	29-Jun-26	0.00					
Testing and Finishes		6	15-Sep-26	21-Sep-26	08-Jul-26	14-Jul-26	0.00					
PRO-SD-PO-120	Issuance of Purchase Order for Manhole Covers of Storm Drainage Network	6	15-Sep-26	21-Sep-26	08-Jul-26	14-Jul-26	0.00					
PRO-SD-PO-140	Issuance of Purchase Order for Catch Basin Covers of Storm Drainage Network	6	15-Sep-26	21-Sep-26	08-Jul-26	14-Jul-26	0.00					
Manufacturing of Material		104	18-Sep-26	30-Dec-26	30-Jun-26	22-Oct-26	0.00					
Main Line Sections		44	18-Sep-26	01-Nov-26	30-Jun-26	08-Aug-26	0.00					
PRO-SD-MF-110	Manufacturing of Materials for Main Line Pipes of Storm Drainage Network	8	18-Sep-26	25-Sep-26	01-Jul-26	09-Jul-26	0.00					
PRO-SD-MF-100	Manufacturing of Materials for Manholes of Storm Drainage Network	40	22-Sep-26	01-Nov-26	30-Jun-26	08-Aug-26	0.00					
Catch Basin Sections		20	22-Sep-26	11-Oct-26	30-Jun-26	19-Jul-26	0.00					
PRO-SD-MF-130	Manufacturing of Materials for Catch Basins of Storm Drainage Network	20	22-Sep-26	11-Oct-26	30-Jun-26	19-Jul-26	0.00					
PRO-SD-MF-150	Manufacturing of Materials for Catch Basin Pipes of Storm Drainage Network	20	22-Sep-26	11-Oct-26	30-Jun-26	19-Jul-26	0.00					
Testing and Finishes		100	22-Sep-26	30-Dec-26	15-Jul-26	22-Oct-26	0.00					
PRO-SD-MF-120	Manufacturing of Materials for Manhole Covers of Storm Drainage Network	100	22-Sep-26	30-Dec-26	15-Jul-26	22-Oct-26	0.00					
PRO-SD-MF-140	Manufacturing of Materials for Catch Basin Covers of Storm Drainage Network	100	22-Sep-26	30-Dec-26	15-Jul-26	22-Oct-26	0.00					
1st Material Delivery & Site Inspection		6	26-Sep-26	01-Oct-26	09-Jul-26	16-Jul-26	0.00					
Main Line Sections		6	26-Sep-26	01-Oct-26	09-Jul-26	16-Jul-26	0.00					
PRO-SD-1DL-110	1ST Material Delivery for Main Line Pipes of Storm Drainage Network	6	26-Sep-26	01-Oct-26	09-Jul-26	16-Jul-26	0.00					
Material Delivery & Site Inspection		20	02-Aug-26 A	01-Nov-26	16-Jul-26	09-Aug-26	0.00					
Main Line Sections		20	02-Aug-26 A	01-Nov-26	16-Jul-26	09-Aug-26	0.00					
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Manholes of Storm Drainage Network	0	02-Aug-26 A	01-Nov-26	09-Aug-26	09-Aug-26	0.00					
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Main Line Pipes of Storm Drainage Network	0	02-Aug-26 A	03-Oct-26	16-Jul-26	16-Jul-26	0.00					
Catch Basin Sections		0	02-Aug-26 A	19-Oct-26	27-Jul-26	27-Jul-26	0.00					
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Catch Basins for Storm Drainage Network	0	02-Aug-26 A	19-Oct-26	27-Jul-26	27-Jul-26	0.00					
PRO-R25-SD-DL-1	Material Delivery & Site Inspection of Catch Basin Pipes for Storm Drainage Network	0	02-Aug-26 A	19-Oct-26	27-Jul-26	27-Jul-26	0.00					
Potable Water Network		104	02-Aug-26 A	15-Jan-27	01-Jul-26	06-Nov-26	0.00					
Issuance of Purchase Orders		10	15-Sep-26	27-Sep-26	01-Jul-26	19-Jul-26	0.00					
Main Line Sections		8	15-Sep-26	24-Sep-26	01-Jul-26	14-Jul-26	0.00					
PRO-PW-PO-110	Issuance of Purchase Order for Valves of Potable Water Network	6	15-Sep-26	21-Sep-26	08-Jul-26	14-Jul-26	0.00					
PRO-PW-PO-100_	Issuance of Purchase Order for Main Line Pipes of Potable Water Network(Remainin	5	19-Sep-26	24-Sep-26	01-Jul-26	07-Jul-26	0.00					
Fire Hydrant		10	15-Sep-26	27-Sep-26	08-Jul-26	19-Jul-26	0.00					
PRO-PW-PO-120	Issuance of Purchase Order for Fire Hydrants of Potable Water Network	10	15-Sep-26	27-Sep-26	08-Jul-26	19-Jul-26	0.00					
Testing and Finishes		10	15-Sep-26	27-Sep-26	08-Jul-26	19-Jul-26	0.00					
PRO-PW-PO-130	Issuance of Purchase Order for Surface Box of Potable Water Network	10	15-Sep-26	27-Sep-26	08-Jul-26	19-Jul-26	0.00					
Manufacturing of Material		116	22-Sep-26	15-Jan-27	07-Jul-26	06-Nov-26	0.00					
Main Line Sections		100	22-Sep-26	30-Dec-26	07-Jul-26	12-Oct-26	0.00					
PRO-PW-MF-110	Manufacturing of Valves for Potable Water Network	90	22-Sep-26	20-Dec-26	15-Jul-26	12-Oct-26	0.00					
PRO-PW-MF-100_	Manufacturing of Main Line Pipes for Potable Water Network(Remaining)	97	25-Sep-26	30-Dec-26	07-Jul-26	11-Oct-26	0.00					
Fire Hydrant		60	28-Sep-26	26-Nov-26	20-Jul-26	17-Sep-26	0.00					
PRO-PW-MF-120	Manufacturing of Fire Hydrants for Potable Water Network	60	28-Sep-26	26-Nov-26	20-Jul-26	17-Sep-26	0.00					

 Primary Baseline
  Actual Work
  Summary
  Remaining Work
  Baseline Milestone
  Critical Remaining Work
  Milestone

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost	2026				
								Aug	Sep	Oct	Nov	Dec
Testing and Finishes		110	28-Sep-26	15-Jan-27	20-Jul-26	06-Nov-26	0.00					
PRO-PW-MF-130	Manufacturing for Surface Box of Potable Water Network	110	28-Sep-26	15-Jan-27	20-Jul-26	06-Nov-26	0.00					
1st Material Delivery & Site Inspection		71	26-Sep-26	16-Dec-26	07-Jul-26	28-Sep-26	0.00					
Main Line Sections		71	26-Sep-26	16-Dec-26	07-Jul-26	28-Sep-26	0.00					
PRO-PW-1DL-100	1ST Material Delivery for Main Line Pipes of Potable Water Network(Remaining)	71	26-Sep-26	16-Dec-26	07-Jul-26	28-Sep-26	0.00					
Material Delivery & Site Inspection		0	02-Aug-26 A	16-Dec-26	29-Sep-26	29-Sep-26	0.00					
Main Line Sections		0	02-Aug-26 A	16-Dec-26	29-Sep-26	29-Sep-26	0.00					
PRO-R25-PW-DL-	Material Delivery & Site Inspection of Main Line Pipes for Potable Water Network(Re	0	02-Aug-26 A	16-Dec-26	29-Sep-26	29-Sep-26	0.00					
Irrigation Network		83	22-Sep-26	28-Dec-26	07-Jul-26	19-Oct-26	0.00					
Issuance of Purchase Orders		6	22-Sep-26	29-Sep-26	07-Jul-26	21-Jul-26	0.00					
Main Line Pipes		6	22-Sep-26	29-Sep-26	07-Jul-26	21-Jul-26	0.00					
PRO-IR-PO-110	Issuance of Purchase Order for Valves of Irrigation Network	6	22-Sep-26	29-Sep-26	15-Jul-26	21-Jul-26	0.00					
PRO-IR-PO-100_R	Issuance of Purchase Order for Main Line Pipes of Irrigation Network(Remaining)	3	26-Sep-26	29-Sep-26	07-Jul-26	11-Jul-26	0.00					
Manufacturing of Material		91	29-Sep-26	28-Dec-26	11-Jul-26	19-Oct-26	0.00					
Main Line Pipes		91	29-Sep-26	28-Dec-26	11-Jul-26	19-Oct-26	0.00					
PRO-IR-MF-100	Manufacturing of Main Line Pipes for Irrigation Network	86	29-Sep-26	24-Dec-26	11-Jul-26	05-Oct-26	0.00					
PRO-IR-MF-110	Manufacturing of Valves for Irrigation Network	90	30-Sep-26	28-Dec-26	22-Jul-26	19-Oct-26	0.00					
Treated Sewage Effluent (Tse)		82	02-Aug-26 A	28-Dec-26	27-Jun-26	10-Oct-26	0.00					
Issuance of Purchase Orders		6	15-Sep-26	21-Sep-26	27-Jun-26	04-Jul-26	0.00					
Main Line Pipes		6	15-Sep-26	21-Sep-26	27-Jun-26	04-Jul-26	0.00					
PRO-TSE-PO-120	Issuance of Purchase Order for Main Line Pipes of Treated Sewage Effluent (Tse)	6	15-Sep-26	21-Sep-26	27-Jun-26	04-Jul-26	0.00					
PRO-TSE-PO-130	Issuance of Purchase Order for Valves of Treated Sewage Effluent (Tse)	6	15-Sep-26	21-Sep-26	27-Jun-26	04-Jul-26	0.00					
Manufacturing of Material		90	22-Sep-26	20-Dec-26	04-Jul-26	02-Oct-26	0.00					
Main Line Pipes		90	22-Sep-26	20-Dec-26	04-Jul-26	02-Oct-26	0.00					
PRO-TSE-MF-120	Manufacturing of Main Line Pipes for Treated Sewage Effluent (Tse)	90	22-Sep-26	20-Dec-26	04-Jul-26	02-Oct-26	0.00					
PRO-TSE-MF-130	Manufacturing of Valves for Treated Sewage Effluent (Tse)	90	22-Sep-26	20-Dec-26	04-Jul-26	02-Oct-26	0.00					
Material Delivery & Site Inspection		0	02-Aug-26 A	28-Dec-26	10-Oct-26	10-Oct-26	0.00					
Main Line Pipes		0	02-Aug-26 A	28-Dec-26	10-Oct-26	10-Oct-26	0.00					
PRO-R25-TSE-DL-	Material Delivery & Site Inspection of Main Line Pipes for Treated Sewage Effluent (T	0	02-Aug-26 A	28-Dec-26	10-Oct-26	10-Oct-26	0.00					
Medium Voltage Network		89	15-Sep-26	28-Dec-26	23-Jun-26	19-Oct-26	0.00					
Issuance of Purchase Orders		12	15-Sep-26	29-Sep-26	23-Jun-26	21-Jul-26	0.00					
Cabling Works		12	15-Sep-26	29-Sep-26	23-Jun-26	06-Jul-26	0.00					
PRO-MV-PO-100	Issuance of Purchase Order for Medium Voltage Cables of Medium Voltage Network	12	15-Sep-26	29-Sep-26	23-Jun-26	06-Jul-26	0.00					
Termination and Testing Works		12	15-Sep-26	29-Sep-26	08-Jul-26	21-Jul-26	0.00					
PRO-MV-PO-120	Issuance of Purchase Order for Termination and Joints Kits of Medium Voltage Netw	12	15-Sep-26	29-Sep-26	08-Jul-26	21-Jul-26	0.00					
Manufacturing of Material		90	30-Sep-26	28-Dec-26	07-Jul-26	19-Oct-26	0.00					
Cabling Works		60	30-Sep-26	28-Nov-26	07-Jul-26	04-Sep-26	0.00					
PRO-MV-MF-100	Manufacturing of Medium Voltage Cables for Medium Voltage Network	60	30-Sep-26	28-Nov-26	07-Jul-26	04-Sep-26	0.00					
Termination and Testing Works		90	30-Sep-26	28-Dec-26	22-Jul-26	19-Oct-26	0.00					
PRO-MV-MF-110	Manufacturing of Termination and Joints Kits for Medium Voltage Network	90	30-Sep-26	28-Dec-26	22-Jul-26	19-Oct-26	0.00					
Low Voltage and Street Lighting Network		132	15-Sep-26	20-Feb-27	23-Jun-26	12-Dec-26	0.00					
Issuance of Purchase Orders		10	15-Sep-26	27-Sep-26	23-Jun-26	06-Aug-26	0.00					
Cabling Works		6	15-Sep-26	21-Sep-26	23-Jun-26	29-Jun-26	0.00					
PRO-SL-PO-100	Issuance of Purchase Order for Lighting Cables of Street Lighting Network	6	15-Sep-26	21-Sep-26	23-Jun-26	29-Jun-26	0.00					
Lighting Poles Works		6	15-Sep-26	21-Sep-26	23-Jun-26	06-Aug-26	0.00					
PRO-SL-PO-110	Issuance of Purchase Order for Lighting Poles Foundations of Street Lighting Netwoi	6	15-Sep-26	21-Sep-26	23-Jun-26	29-Jun-26	0.00					
PRO-SL-PO-120	Issuance of Purchase Order for Lighting Poles of Street Lighting Network	6	15-Sep-26	21-Sep-26	23-Jun-26	29-Jun-26	0.00					
PRO-SL-PO-140	Issuance of Purchase Order for Lighting Fixtures of Street Lighting Network	6	15-Sep-26	21-Sep-26	01-Aug-26	06-Aug-26	0.00					
Distribution Panel Board		10	15-Sep-26	27-Sep-26	23-Jun-26	04-Jul-26	0.00					
PRO-SL-PO-160	Issuance of Purchase Order for Distrubution Panel Boards of Street Lighting Network	10	15-Sep-26	27-Sep-26	23-Jun-26	04-Jul-26	0.00					
Termination and Testing Works		8	15-Sep-26	24-Sep-26	08-Jul-26	16-Jul-26	0.00					
PRO-SL-PO-130	Issuance of Purchase Order for Fuse Boxes of Street Lighting Network	8	15-Sep-26	24-Sep-26	08-Jul-26	16-Jul-26	0.00					
PRO-SL-PO-170	Issuance of Purchase Order for Cable Lugs of Street Lighting Network	8	15-Sep-26	24-Sep-26	08-Jul-26	16-Jul-26	0.00					

 Primary Baseline
  Actual Work
  Summary
  Remaining Work
  Baseline Milestone
  Critical Remaining Work
  Milestone

ansab		Development of the Technology City in Dammam-Project UPDATE 15-09-2026 3Week Lookahead Schedule					egis		MODON مَدِينَة الرياض			
Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost	2026				
								Aug	Sep	Oct	Nov	Dec
Earthing System Works		8	15-Sep-26	24-Sep-26	07-Jul-26	15-Jul-26	0.00					
PRO-SL-PO-150	Issuance of Purchase Order for Lighting Earthing of Street Lighting Network	8	15-Sep-26	24-Sep-26	07-Jul-26	15-Jul-26	0.00					
Manufacturing of Material		152	22-Sep-26	20-Feb-27	30-Jun-26	12-Dec-26	0.00					
Cabling Works		90	22-Sep-26	20-Dec-26	30-Jun-26	27-Sep-26	0.00					
PRO-SL-MF-100	Manufacturing of Lighting Cables for Street Lighting Network	90	22-Sep-26	20-Dec-26	30-Jun-26	27-Sep-26	0.00					
Lighting Poles Works		128	22-Sep-26	27-Jan-27	30-Jun-26	12-Dec-26	0.00					
PRO-SL-MF-110	Manufacturing of Lighting Poles Foundations for Street Lighting Network	90	22-Sep-26	20-Dec-26	30-Jun-26	27-Sep-26	0.00					
PRO-SL-MF-120	Manufacturing of Lighting Poles for Street Lighting Network	90	22-Sep-26	20-Dec-26	30-Jun-26	27-Sep-26	0.00					
PRO-SL-MF-140	Manufacturing of Lighting Fixtures for Street Lighting Network	128	22-Sep-26	27-Jan-27	07-Aug-26	12-Dec-26	0.00					
Distribution Panel Board		110	28-Sep-26	15-Jan-27	05-Jul-26	22-Oct-26	0.00					
PRO-SL-MF-160	Manufacturing of Distrubution Panel Boards for Street Lighting Network	110	28-Sep-26	15-Jan-27	05-Jul-26	22-Oct-26	0.00					
Termination and Testing Works		149	25-Sep-26	20-Feb-27	17-Jul-26	12-Dec-26	0.00					
PRO-SL-MF-130	Manufacturing of Fuse Boxes for Street Lighting Network	149	25-Sep-26	20-Feb-27	17-Jul-26	12-Dec-26	0.00					
PRO-SL-MF-170	Manufacturing of Cable Lugs for Street Lighting Network	110	25-Sep-26	12-Jan-27	17-Jul-26	03-Nov-26	0.00					
Earthing System Works		140	25-Sep-26	11-Feb-27	16-Jul-26	02-Dec-26	0.00					
PRO-SL-MF-150	Manufacturing of Lighting Earthing for Street Lighting Network	140	25-Sep-26	11-Feb-27	16-Jul-26	02-Dec-26	0.00					
Telecom Network		82	15-Sep-26	20-Dec-26	07-Jul-26	11-Oct-26	0.00					
Issuance of Purchase Orders		6	15-Sep-26	21-Sep-26	07-Jul-26	13-Jul-26	0.00					
Ducts Works		6	15-Sep-26	21-Sep-26	07-Jul-26	13-Jul-26	0.00					
PRO-TE-PO-100	Issuance of Purchase Order for Ducts forTelecom Network	6	15-Sep-26	21-Sep-26	07-Jul-26	13-Jul-26	0.00					
Manholes Works		6	15-Sep-26	21-Sep-26	07-Jul-26	13-Jul-26	0.00					
PRO-TE-PO-110	Issuance of Purchase Order for Manholes forTelecom Network	6	15-Sep-26	21-Sep-26	07-Jul-26	13-Jul-26	0.00					
CCTV System Wroks		6	15-Sep-26	21-Sep-26	07-Jul-26	13-Jul-26	0.00					
PRO-CTV-PO-100	Issuance of Purchase Order for Civil and Finishes Works of CCTV Complete System	6	15-Sep-26	21-Sep-26	07-Jul-26	13-Jul-26	0.00					
Manufacturing of Material		90	22-Sep-26	20-Dec-26	14-Jul-26	11-Oct-26	0.00					
Ducts Works		60	22-Sep-26	20-Nov-26	14-Jul-26	11-Sep-26	0.00					
PRO-TE-MF-100	Manufacturing of Ducts for Telecom Network	60	22-Sep-26	20-Nov-26	14-Jul-26	11-Sep-26	0.00					
Manholes Works		90	22-Sep-26	20-Dec-26	14-Jul-26	11-Oct-26	0.00					
PRO-TE-MF-110	Manufacturing of Manholes for Telecom Network	90	22-Sep-26	20-Dec-26	14-Jul-26	11-Oct-26	0.00					
CCTV System Wroks		90	22-Sep-26	20-Dec-26	14-Jul-26	11-Oct-26	0.00					
PRO-CTV-MF-100	Manufacturing of Civil and Finishes Works for CCTV Complete System	90	22-Sep-26	20-Dec-26	14-Jul-26	11-Oct-26	0.00					
Superstructure Works		121	02-Aug-26 A	13-Dec-26	23-Jun-26	11-Oct-26	0.00					
Issuance of Purchase Orders		18	15-Sep-26	06-Oct-26	23-Jun-26	13-Jul-26	0.00					
Storage Tank (TSE)		11	24-Sep-26	06-Oct-26	01-Jul-26	13-Jul-26	0.00					
PRO-TSE-CV-PO-30	Issuance of Purchase Order for Civil Works for Storage Tank (TSE)	11	24-Sep-26	06-Oct-26	01-Jul-26	13-Jul-26	0.00					
Gaurd Room		11	15-Sep-26	28-Sep-26	23-Jun-26	05-Jul-26	0.00					
PRO-GR-CV-PO-40	Issuance of Purchase Order for Civil Works for Gaurd Room	11	15-Sep-26	28-Sep-26	23-Jun-26	05-Jul-26	0.00					
Manufacturing of Material		90	15-Sep-26	13-Dec-26	23-Jun-26	11-Oct-26	0.00					
Pump Stations		40	15-Sep-26	24-Oct-26	23-Jun-26	01-Aug-26	0.00					
PRO-SPS-CV-MF-10	Manufacturing of Civil Works for Pump Stations	40	15-Sep-26	24-Oct-26	23-Jun-26	01-Aug-26	0.00					
Lift Station		40	15-Sep-26	24-Oct-26	23-Jun-26	01-Aug-26	0.00					
PRO-LS-CV-MF-30	Manufacturing of Civil Works for Civil Works for Lift Stations	40	15-Sep-26	24-Oct-26	23-Jun-26	01-Aug-26	0.00					
Gaurd Room		40	28-Sep-26	07-Nov-26	05-Jul-26	14-Aug-26	0.00					
PRO-GR-CV-MF-50	Manufacturing of Civil Works for Civil Works for Gaurd Room	40	28-Sep-26	07-Nov-26	05-Jul-26	14-Aug-26	0.00					
Softscape and Planting Works		90	15-Sep-26	13-Dec-26	13-Jul-26	11-Oct-26	0.00					
PRO-FE-CV-MF-70	Manufacturing of Civil Works for Softscape and Planting Works	90	15-Sep-26	13-Dec-26	13-Jul-26	11-Oct-26	0.00					
Material Delivery & Site Inspection		9	02-Aug-26 A	05-Nov-26	25-Jul-26	04-Aug-26	0.00					
Pump Stations		0	02-Aug-26 A	05-Nov-26	04-Aug-26	04-Aug-26	0.00					
PRO-SPS-CV-DL-10	Material Delivery & Site Inspection for Civil Works for Pump Stations	0	02-Aug-26 A	05-Nov-26	04-Aug-26	04-Aug-26	0.00					
Fence		0	02-Aug-26 A	15-Sep-26	25-Jul-26	25-Jul-26	0.00					
PRO-FE-CV-DL-80	Material Delivery & Site Inspection for Civil Works for Fence	0	02-Aug-26 A	15-Sep-26	25-Jul-26	25-Jul-26	0.00					
Long Lead Time Items		38	15-Sep-26	29-Oct-26	23-Jun-26	06-Aug-26	0.00					
Infrastructure Networks		20	15-Sep-26	08-Oct-26	23-Jun-26	15-Jul-26	0.00					
								Date	Revision		Checked	Approved
								15-Sep-26	Third Industrial City			

Primary Baseline

Remaining Work

Critical Remaining Work

Actual Work

Baseline Milestone

Milestone

Summary

4/6

Date

15-Sep-26

Revision



Third Industrial City

Checked

Approved



Development of the Technology City in Dammam-Project
UPDATE 15-09-2026
3Week Lookahead Schedule

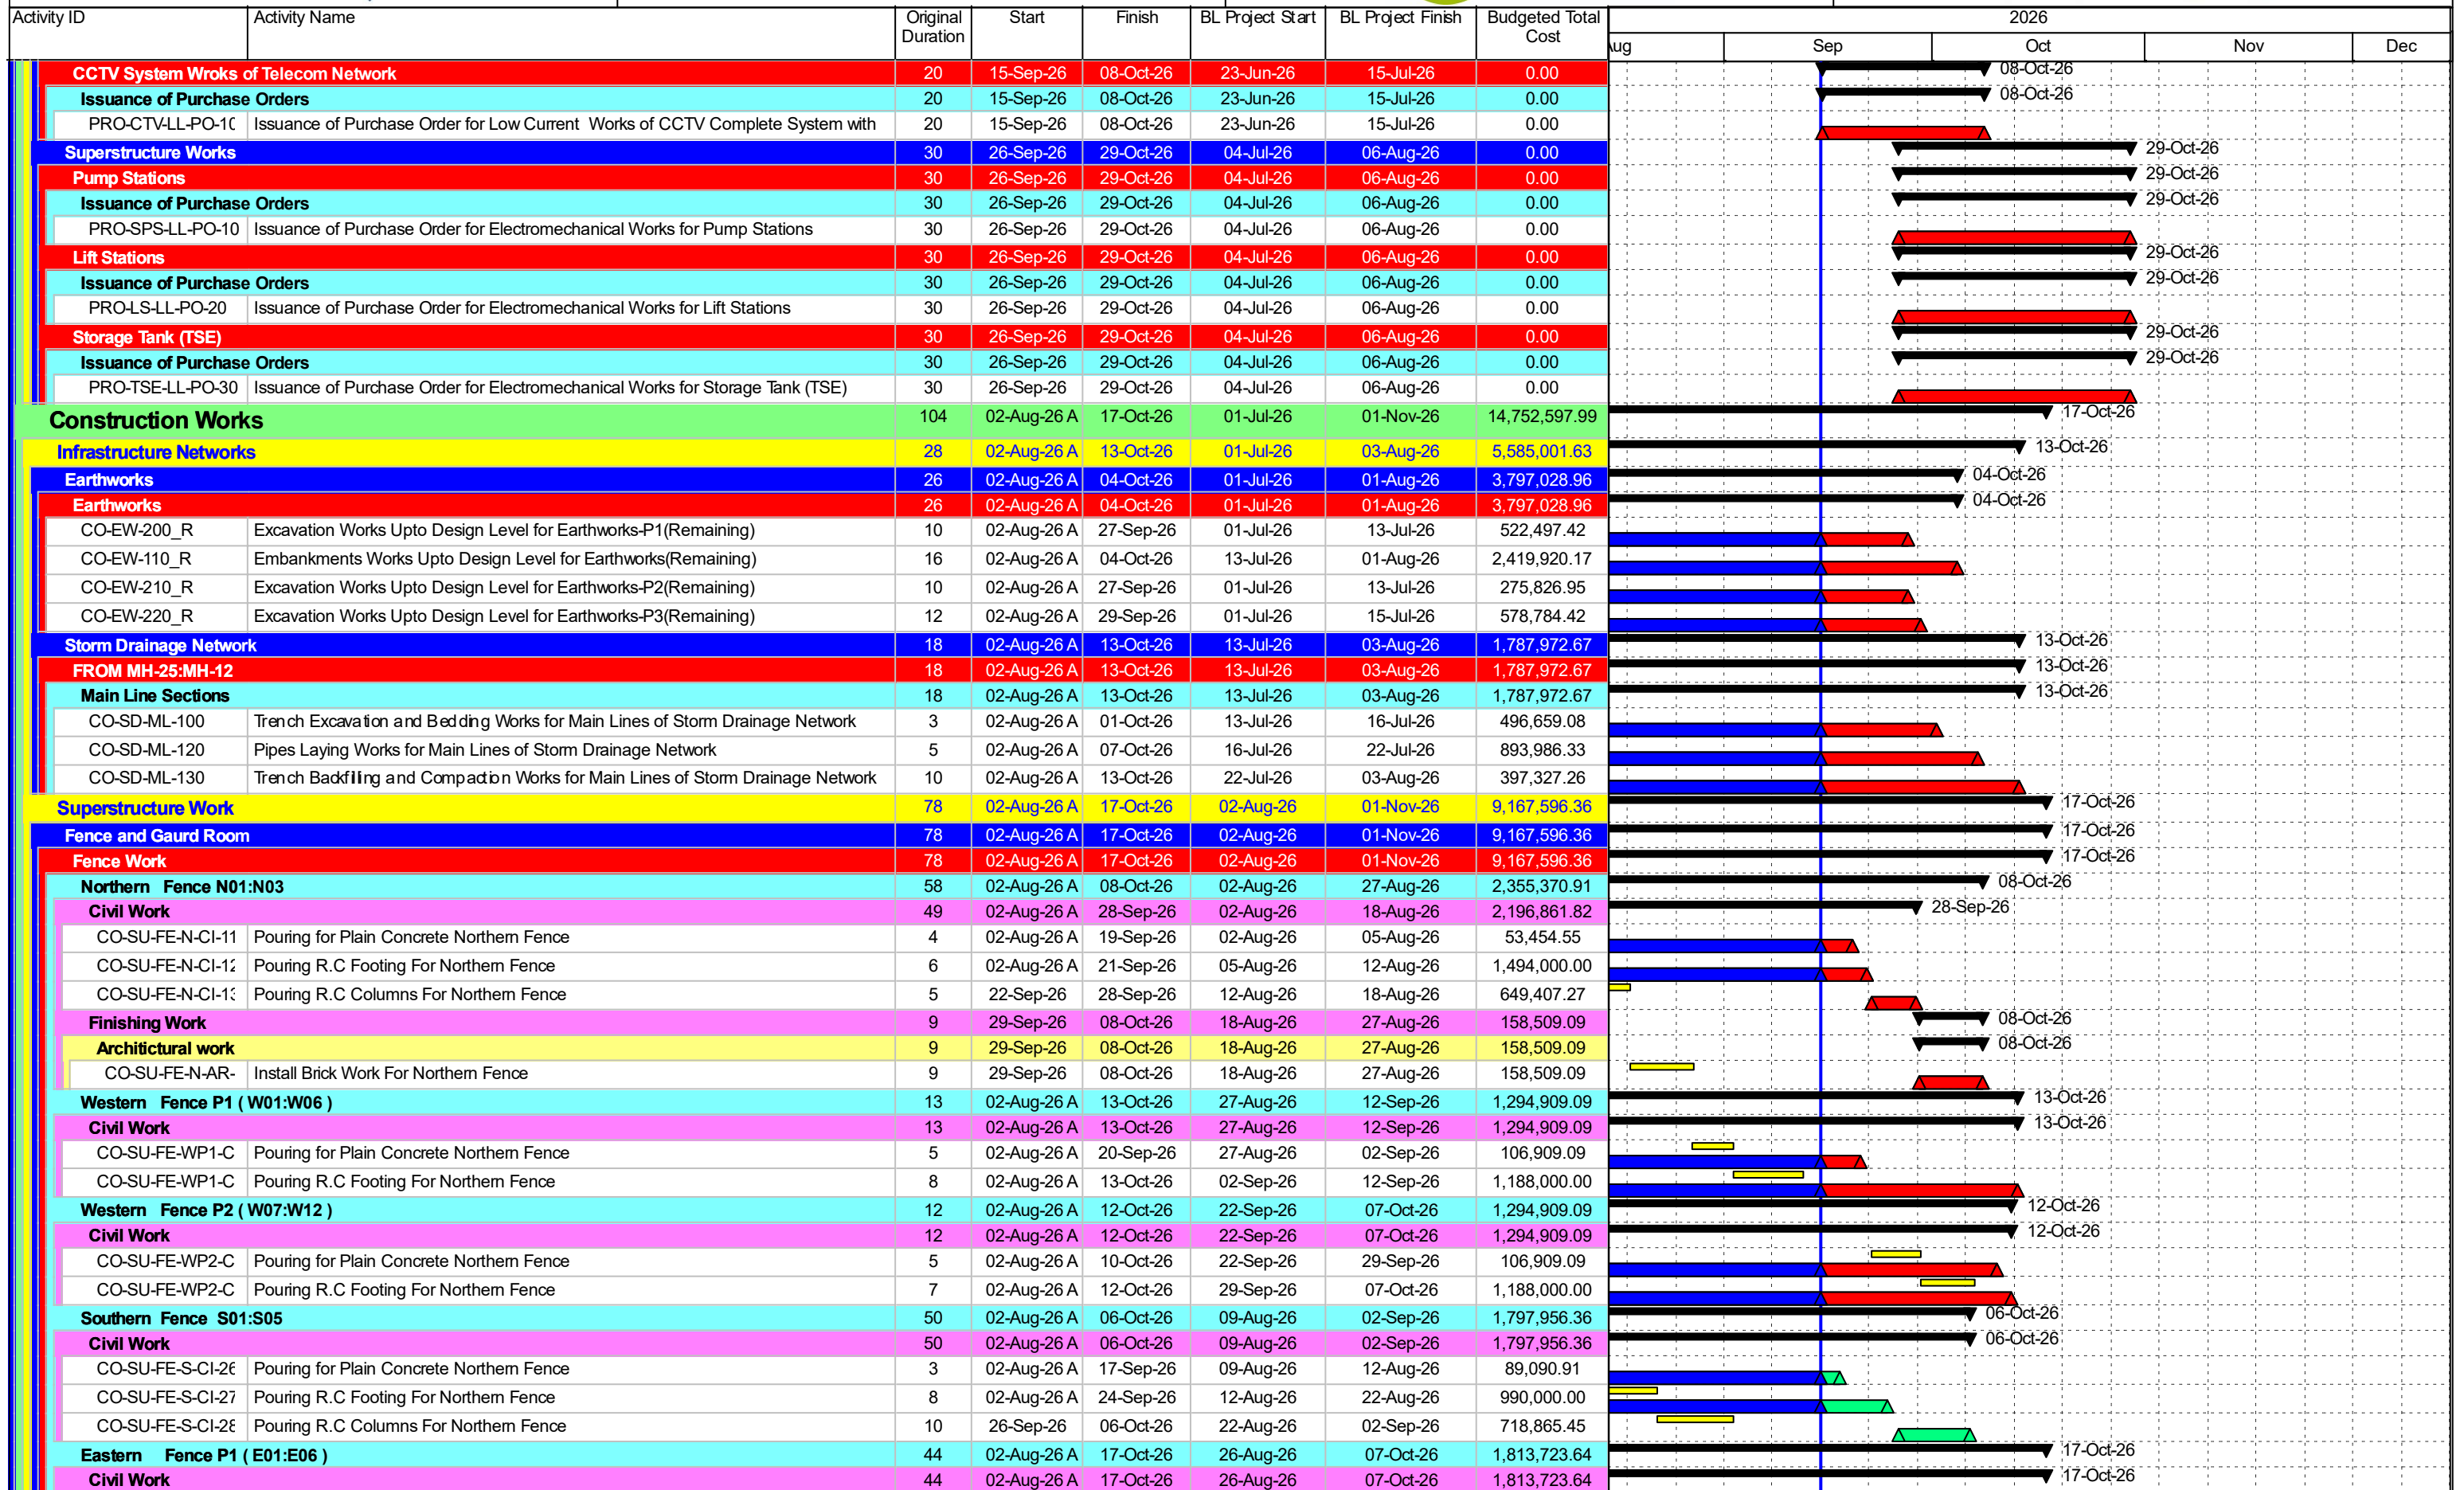

Activity ID		Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Budgeted Total Cost	2026				
									Aug	Sep	Oct	Nov	Dec
10	CO-SU-FE-EP1-CI	Pouring for Plain Concrete Northern Fence	8	02-Aug-26 A	24-Sep-26	26-Aug-26	05-Sep-26	106,909.09					
	CO-SU-FE-EP1-CI	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	29-Sep-26	05-Sep-26	19-Sep-26	1,188,000.00					
	CO-SU-FE-EP1-CI	Pouring R.C Columns For Northern Fence	15	30-Sep-26	17-Oct-26	19-Sep-26	07-Oct-26	518,814.55					
	Eastern Fence P2 (E07:E13)		24	02-Aug-26 A	17-Oct-26	04-Oct-26	01-Nov-26	610,727.27	17-Oct-26				
	Civil Work		24	02-Aug-26 A	17-Oct-26	04-Oct-26	01-Nov-26	610,727.27	17-Oct-26				
	CO-SU-FE-EP2-CI	Pouring for Plain Concrete Northern Fence	12	02-Aug-26 A	17-Oct-26	04-Oct-26	18-Oct-26	124,727.27					
	CO-SU-FE-EP2-CI	Pouring R.C Footing For Northern Fence	12	02-Aug-26 A	17-Oct-26	18-Oct-26	01-Nov-26	486,000.00					
	Testing and Comissioning		0	03-Oct-26	03-Oct-26	04-Jan-27	04-Jan-27	0.00	▼ 03-Oct-26				
	Utility Buildings		0	03-Oct-26	03-Oct-26	04-Jan-27	04-Jan-27	0.00	▼ 03-Oct-26				
	T/C-DPO	Testing and Comissioning of Storm Drainage Ponds	0	03-Oct-26	03-Oct-26	04-Jan-27	04-Jan-27	0.00					
Handing over and close out		14	03-Oct-26	18-Oct-26	04-Jan-27	19-Jan-27	0.00	18-Oct-26					
As-Built		14	03-Oct-26	18-Oct-26	04-Jan-27	19-Jan-27	0.00	18-Oct-26					
HO-130	Submission As-Built Drawing For Pond	14	03-Oct-26	18-Oct-26	04-Jan-27	19-Jan-27	0.00						
